

TAHOE*TRUCKEE UNIFIED SCHOOL DISTRICT

PATHWAYS TO POSSIBILITIES AND STUDENT SUCCESS

Facilities Bond Program Update

February 24, 2021 Board of Education Meeting

JORGE ROJAS

DIRECTOR OF FACILITIES, MAINTENANCE, AND OPERATIONS





Measure U

2015 Projects:

- Truckee High School- Track and Restroom Completed
- Glenshire Elementary School- Parking Lot Reconfiguration Completed

2016 Projects:

- Alder Creek Middle School- Parking Lot Reconfiguration -Completed
- Glenshire Elementary School- Modernization Completed
- Sierra High School- Modernization Completed
- SELS- Parking Lot Reconfiguration Completed









Measure U

2017 Projects:

- New Maintenance/Warehouse Facility Completed
- Truckee High School- West Wing and Site Work Completed
- Donner Trail Elementary School- New Construction/Modernization -Completed

2018-2020 Projects:

- Truckee Elementary School- New Construction/Modernization Completed
- Truckee Elementary School- Reroof— Completed
- Truckee High School- Increment 2- Modernization of Existing Building - Completed










Measure U

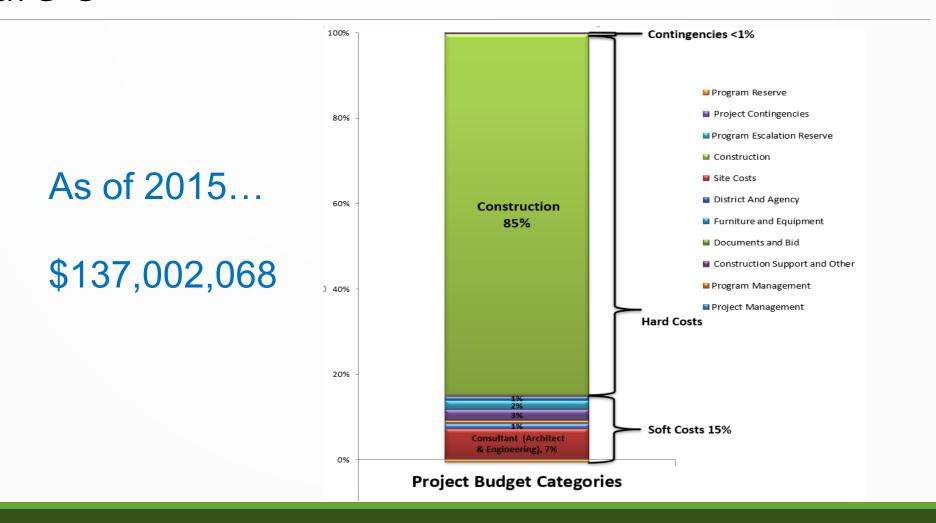









- ➤ Inc. 1-Construction completion August 2018
- ➤ Inc. 2-Start of construction July 2019
- ➤ Inc. 2-Construction completion scheduled for November 2020
- Project Architect: DLR Group
- TTUSD Project Manager: Rob Koster
- Inc. 2 Lease Leaseback Entity: CORE Construction
- Revised Construction Budget: \$72,706,505
- Revised Total Budget: \$82,237,129





Truckee High School A look back....













Truckee High School A look back....














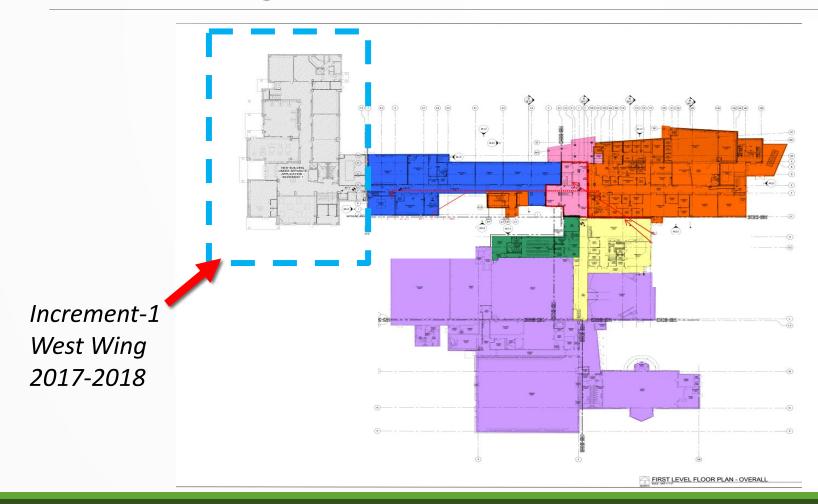



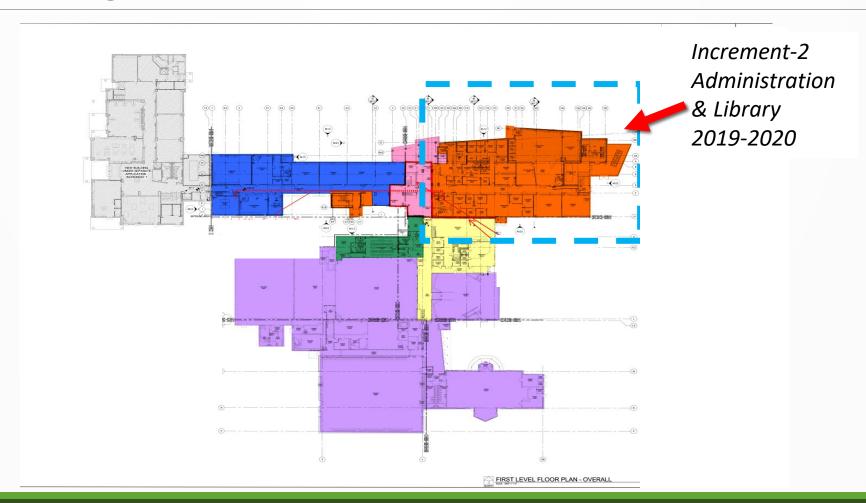




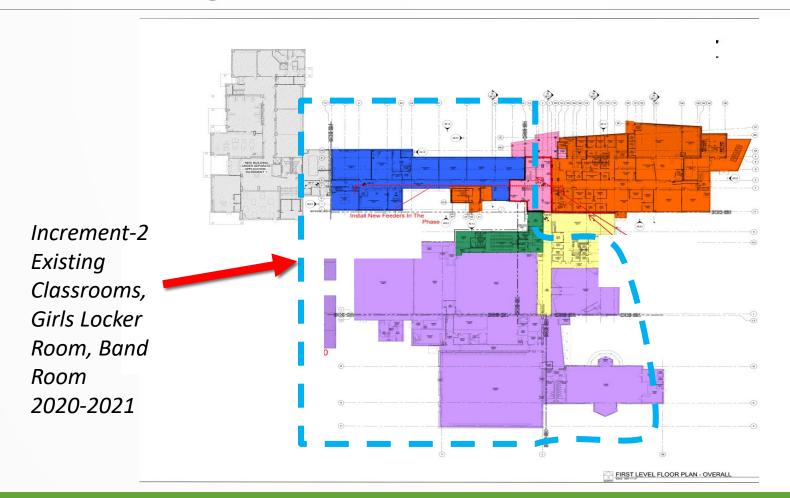




- Culinary Arts Lab
- Wellness Center
- Coldstream Science Lab
- Life Skills Classroom
- Student Commons Area
- New Stair Tower
- (10) General Classrooms
- Girls Locker Room
- Expanded Band Room
- New Green Room











Progress Pictures May 20, 2020











- Fire Alarm System Upgrades
- 21st Century Technology Voice Amplification System, Digital Clock Speaker, and TV Cart
- Mechanical Upgrades Heating and Cooling
- ADA Access compliance
















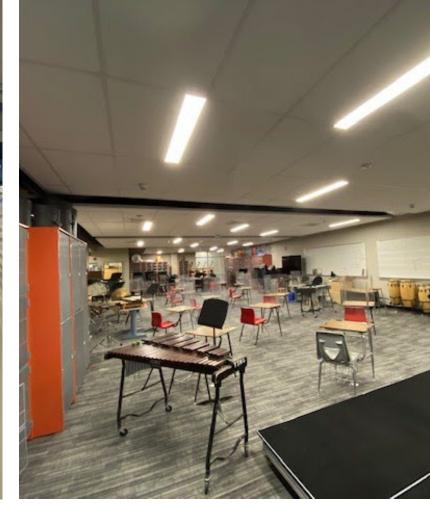



















LLB Project Close Out

- Division of State Architect Certification
- Finalize project costs (GMP)
- Revise LLB entity fee
- Complete Memorandum of Commencement (MOC)
- Start of Lease term
- Releases and Termination agreement
- Finalize all Furniture Purchases













Measure E

2015-2020 Projects:

- Tahoe Lake Elementary Boiler Replacement -Completed
- Kings Beach Elementary Boiler Replacement -Completed
- North Tahoe School Gym Reroof Completed
- Sierra High School- Modernization Completed
- New Maintenance/Warehouse Facility -Completed











As of 2016...

\$82,909,917

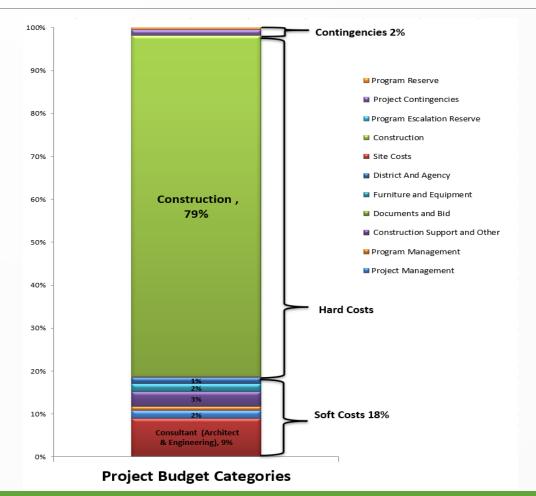

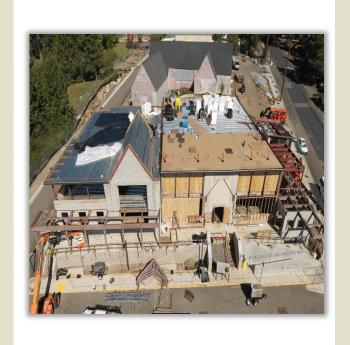








- > Start of construction June 2017
- Construction completed September 2020
- Project Architect: Architectural Nexus
- TTUSD Project Manager: Kristin Hillmer
- Construction Manager: CORE Construction
- Revised Construction Budget: \$40,904,166
- Revised Total Budget: \$49,362,487







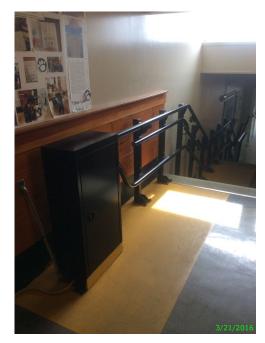





A look back....










A look back....





Progress Pictures May 20, 2020

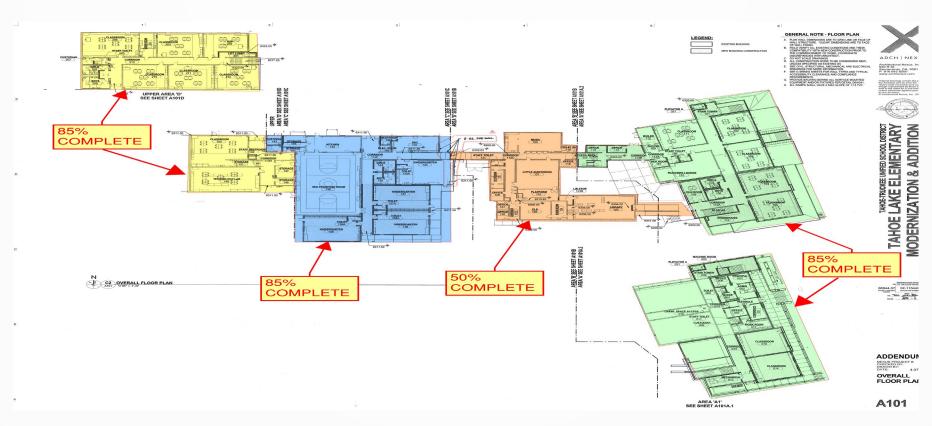







Progress Pictures May 20, 2020

























- Fire Alarm System Upgrades
- 21st Century Technology Voice Amplification System, Digital Clock Speaker, and TV Cart
- Mechanical Upgrades Heating and Cooling

- New Casework and storage
- Blinds
- New Lighting
- Flexible Furniture












- New ADA access lifts and ramps
- Accessible Path of Travel in compliance throughout campus



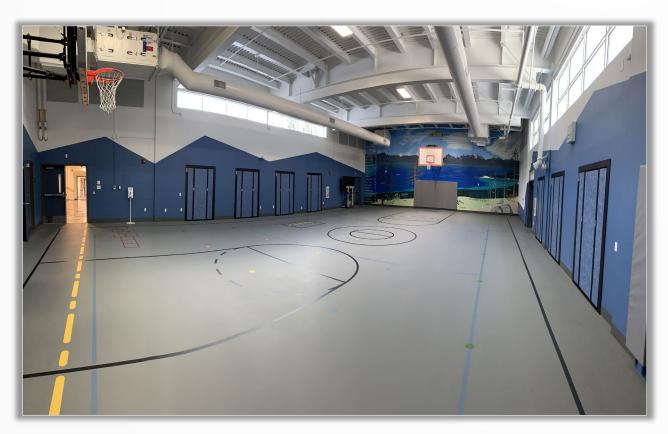





- ModernizedMP Room
- Reconfigured Kitchen and Serving Area











- Structural Repairs
- Waterproofing of Structure
- Insulation and Venting
- Electrical and Low Voltage


















North Tahoe School and High School

Project Architect: TBD

TTUSD Project Manager: TBD

Construction Budget: \$3,823,940





